



**THE UNITED REPUBLIC OF TANZANIA**  
**PRESIDENT'S OFFICE**  
**REGIONAL ADMINISTRATION AND LOCAL GOVERNMENT**  
**NGARA DISTRICT COUNCIL**  
**LOCAL AREA DEVELOPMENT PROGRAM (LADP)**



**TAARIFA YA ZIARA YA MKUU WA WILAYA NGARA KUKAGUA MAENDELEO YA  
UTEKELEZAJI WA MIRADI YA LADP II**

**17<sup>th</sup> February 2024**

# MAENDELEO YA UTEKELEZAJI WA MIRADI YA LADP II

## 01.Ujenzi wa soko la kimkakati la Kahaza Rusumo

**ARCHITECT**

**ARCHVIEW CONSULTS** Architects Planners Interior Designers Project Managers  
CCM Regional Block  
Mwanambao Rd (P.O. Box 253) Moshi, Moshi No. 61, 6 08  
P.O. Box 253, Mwanambao, Tanzania  
@ArchViewConsults | www.archviewconsults.com  
+255 763 967 396 | +255 767 907 391 | +255 697 634 764

**DISTRICT EXECUTIVE DIRECTOR**  
**CLIENT:** NGARA DISTRICT COUNCIL  
P.O.BOX 30, NGARA



**FINANCER:**  
REGIONAL RUSUMO FALLS HYDROELECTRIC POWER PROJECT/ WORLD BANK THROUGH NELSAP UNDER LOCAL AREA DEVELOPMENT PROGRAM (LADP)

**PROJECT:** PROPOSED CONSTRUCTION OF RUSUMO STRATEGIC MARKET CENTRE TO BE BUILT AT KAHAZA

### Sehemu A : Taarifa za mradi

Mkandarasi ni : **Armstrong International Limited.**

Gharama za Mradi ni : **2,517,833,023/=**

Gharama zilizoishalipwa mpaka sasa ni : **786,157,997.40/=**

Kiasi kilichobaki mpaka sasa ni : **1,731,675,025/=**

Aina ya kazi zinazotakiwa kufanyika ni: **Ujenzi wa jengo la soko, ujenzi wa sehemu ya maegesho ya magari ya mizigo, numba za walenzi na uzio wa soko.**

Hatua aliyofikia kwa sasa: **Mkandarasi yupo katika hatua ya kufunga maboksi na kumwaga zege la nguzo, kasi ya maendeleo ni nzuri kwa sasa na mradi unatarajia kukamilika 31/03/2024.**

Asimlimia za utekelezaji ni: **38%**

**Sehemu B : Picha za maendeleo ya mradi kwa sasa.**



**Muonekano wa utekelezaji sehemu ya jengo la soko kwa nje na ndani**



**Muonekano wa utekelezaji sehemu ya jengo la soko kwa nje na ndani**



**Mkuu wa Wilaya Ngara Kanali Mathias J. Kahabi akikagua sehemu ya jengo la soko kwa ndani**



Feb 17, 2024 11:11:35 AM



Feb 17, 2024 11:25:09 AM



**Mkuu wa Wilaya Ngara Kanali Mathias J. Kahabi akisikiliza maelezo ya mkandarasi kuhusu maendeleo ya mradi na changamoto zilizopo.**

## 02.Ujenzi wa jengo la Makao ya ofisi ya Halimashaouri ya Wilaya Ngara.



### **Sehemu A : Taarifa za mradi**

Mkandarasi ni : **Home Africa Investment corporation Limited.**

Gharama za Mradi ni : **3,599,127,670.69/=**

Gharama zilizoishalipwa mpaka sasa ni : **1,000,252,693/=**

Kiasi kilichobaki mpaka sasa ni : **2,598,874,977/=**

Aina ya kazi zinazotakiwa kufanyika ni: **Mkandarasi anatekeleza ujenzi wa jengo la utawala la Halmashauri lenye gorofa moja tu.**

Hatua aliyofikia kwa sasa: **Mkandarasi yupo katika hatua ya kufunga maboksi na kumwaga zege la nguzo mlalo na jamvi la juu pamoja na nondo zake, kasi ya maendeleo ni nzuri kwa sasa na mradi unatarajia kukamilika 31/06/2024.**

Asimlimia za utekelezaji ni: **46%**



**Sehemu B : Picha za maendeleo ya mradi kwa sasa.**



**Mkuu wa Wilaya Ngara Kanali Mathias J. Kahabi akikagua jengo la makao makuu ya Halimashauri ya Wilaya tarehe 17.02.2024.**



**Mkuu wa Wilaya Ngara Kanali Mathias J. Kahabi akikagua jengo la makao makuu ya Halimashauri ya Wilaya Ngara tarehe 17.02.2024.**



**Mkuu wa Wilaya Ngara Kanali Mathias J. Kahabi akikagua jengo la makao makuu ya Halimashauri ya Wilaya Ngara tarehe 17.02.2024.**



**Mkuu wa Wilaya Ngara Kanali Mathias J. Kahabi akikagua jengo la makao makuu ya Halimashauri ya Wilaya Ngara tarehe 17.02.2024.**

### 03.Ujenzi wa Bweni, Jengo la Utawala, Bwalo la chakula na Jiko katika Shule ya Sekondari ya juu ya wanaume Ngara.

FRONT ELEVATION

REAR ELEVATION

RIGHT SIDE ELEVATION

LEFT SIDE ELEVATION

General Notes

No.	Description	Date

CLIENT:  
UNITED REPUBLIC OF TANZANIA  
MINISTRY OF WORKS,  
SPECIAL SERVICES & REGIONAL DEVELOPMENT  
GOVERNMENT  
NGARA DISTRICT COUNCIL

PROJECT:  
LOCAL AREA DEVELOPMENT PROGRAM  
(LADP)  
PROPOSED NGARA RESIDENTIAL  
ADMINISTRATION BUILDING

CONSULTANT:  
**ARCVIEW CONSULTANTS**  
 ARCHITECTS & ENGINEERS  
 P.O. BOX 10000, DAR ES SALAAM, TANZANIA  
 TEL: +255 22 261 1111  
 FAX: +255 22 261 1112  
 WWW.ARCVIEWCONSULTANTS.CO.TZ

Drawing Title  
**ELEVATIONS**

Drawn by: Mwanaliwa M. M.	Checked by: Mwanaliwa M. M.
Date: 2023/05/05	Scale: AS SHOWN
Sheet No: 05	Project No: 05

### JENGO LA UTAWALA PANDE ZOTE

FRONT ELEVATION

REAR ELEVATION

General Notes

No.	Description	Date

CLIENT:  
UNITED REPUBLIC OF TANZANIA  
MINISTRY OF WORKS,  
SPECIAL SERVICES & REGIONAL DEVELOPMENT  
GOVERNMENT  
NGARA DISTRICT COUNCIL


PROJECT:  
LOCAL AREA DEVELOPMENT PROGRAM  
(LADP)  
PROPOSED NGARA RESIDENTIAL  
ADMINISTRATION BUILDING

CONSULTANT:  
**ARCVIEW CONSULTANTS**  
 ARCHITECTS & ENGINEERS  
 P.O. BOX 10000, DAR ES SALAAM, TANZANIA  
 TEL: +255 22 261 1111  
 FAX: +255 22 261 1112  
 WWW.ARCVIEWCONSULTANTS.CO.TZ

Drawing Title  
**ELEVATIONS**

Drawn by: Mwanaliwa M. M.	Checked by: Mwanaliwa M. M.
Date: 2023/05/05	Scale: AS SHOWN
Sheet No: 05	Project No: 05

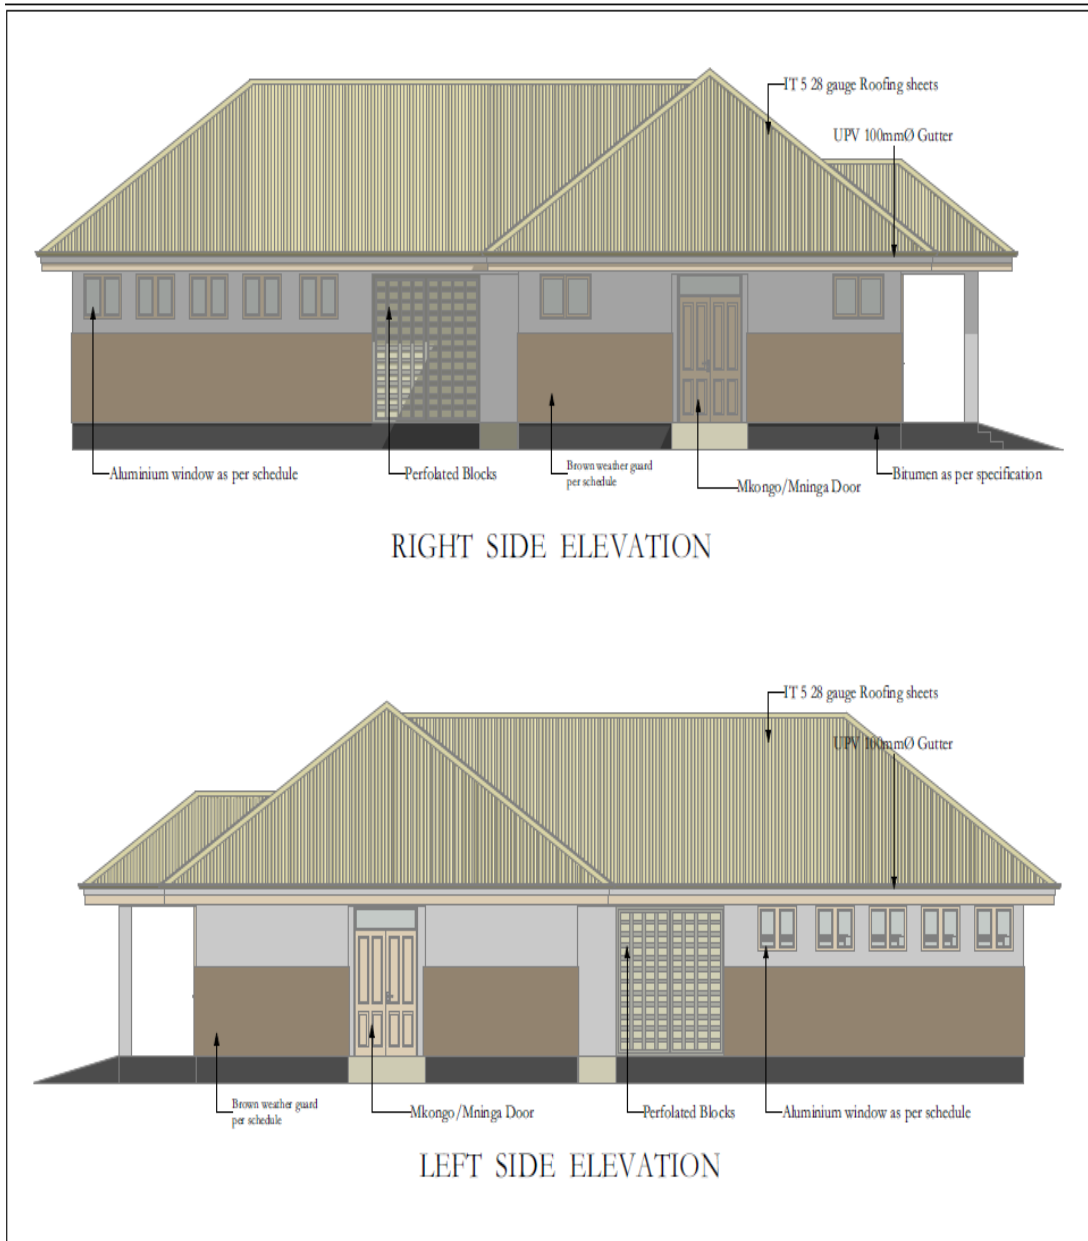

### BWENI UPANDE WA MBELE NA NYUMA




RIGHT SIDE ELEVATION

LEFT SIDE ELEVATION

General Notes

No.	Revisions/Date	Date
CLIENT: UNITED REPUBLIC OF TANZANIA PRESIDENT'S OFFICE REGIONAL ADMINISTRATION AND LOCAL GOVERNMENT NGARA DISTRICT COUNCIL		
		
PROJECT: LOCAL AREA DEVELOPMENT PROGRAM (LADP) PROPOSED DOMITORY AT NGARA HIGH SCHOOL		
CONSULTANT: 		
Drawing Title <b>ELEVATIONS</b>		
Drawn by: Kwamb. W. & G. S. S.	Checked by: Vanisia Mwangi (Reg. Archt)	
	Approved by: Zakaria Mwanza (Reg. Archt)	
Date: June 2022	Drawn No: AVC/2022-001/AR/07-16	Sheet No: 06
Scale: AS SHOWN		

**BWENI UPANDE WA KULIA NA KUSHOTO**

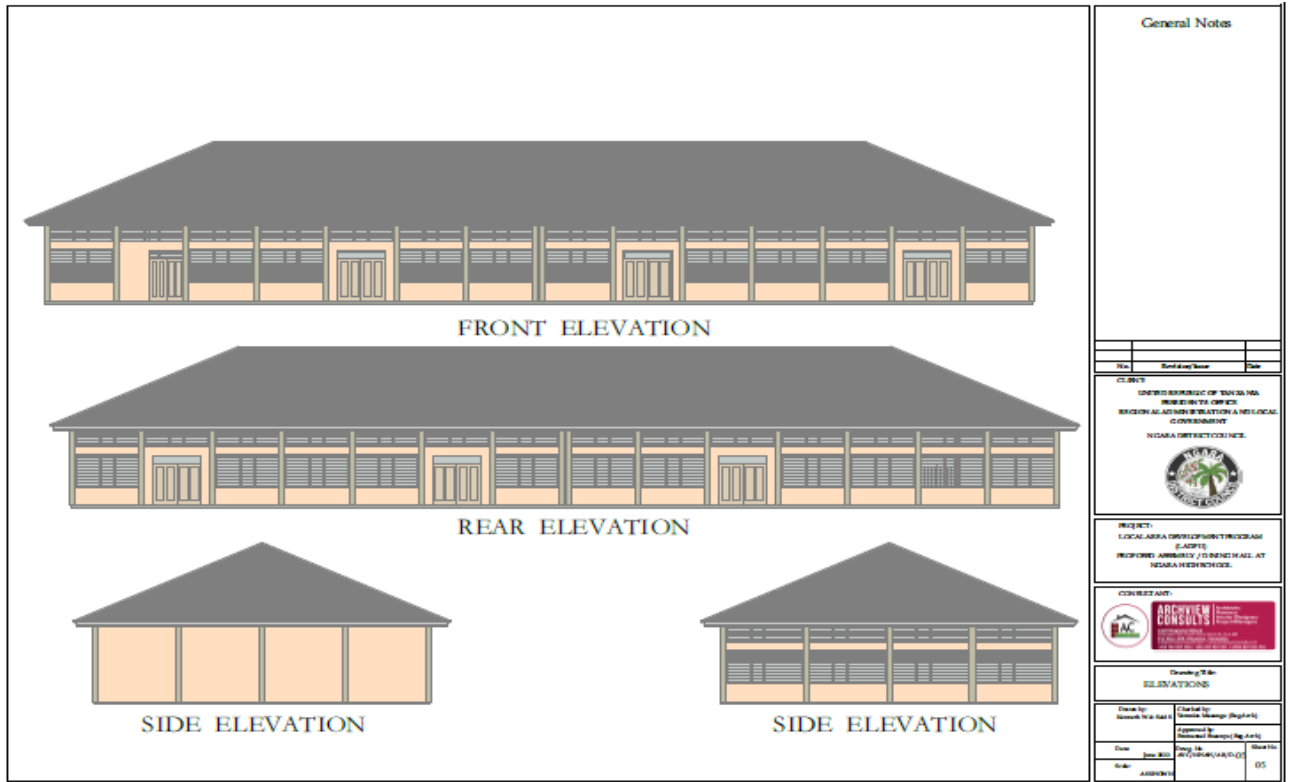

**BWALO LA CHAKULA PANDE ZOTE NNE**

**Sehemu A : Taarifa za mradi**

Mkandarasi ni : **Gesap Engineering Group.**

Gharama za Mradi ni : **1,287,528,500/=**

Gharama zilizoishalipwa mpaka sasa ni : **438,176,053.70/=**

Kiasi kilichobaki mpaka sasa ni : **849,352,446/=**

Aina ya kazi zinazotakiwa kufanyika ni: **Ujenzi wa jengo la Bweni, Bwaro na Jiko la chakula pamoja na Jengo la Utawala.**

Hatua aliyofikia kwa sasa: **Mkandarasi yupo katika hatua ya kumwaga zege la nguzo wima na mlalo za juu pamoja na nondo zake, pia kwenye bweni youpo tayari kuweka kenchi za paa, kasi ya maendeleo siyo nzuri kwa sasa kuna kazi zimesimama kutokana na kutokuwepo kwa mchanga na kokoto za kutosha eneo la kazi na mradi unatarajiwa kukamilika 31/03/2024.**

Asimlimia za utekelezaji ni: **55.6%**

**Sehemu B : Picha za maendeleo ya mradi kwa sasa.**



**Mkuu wa Wilaya Ngara Kanali Mathias J. Kahabi akikagua jengo la Bwalo la chakula katika shule ya sekondari ya juu ya wanaume Ngara tarehe 17.02.2024.**





**Mkuu wa Wilaya Ngara Kanali Mathias J. Kahabi akikagua jengo la Bwalo la chakula katika shule ya sekondari ya juu ya wanaume Ngara tarehe 17.02.2024.**

**<MWISHO>**

**Imeandaliwa na: SUBIRA SIMON.**

**MUHANDISI WA MIRADI LADP NGARA DC.**
